
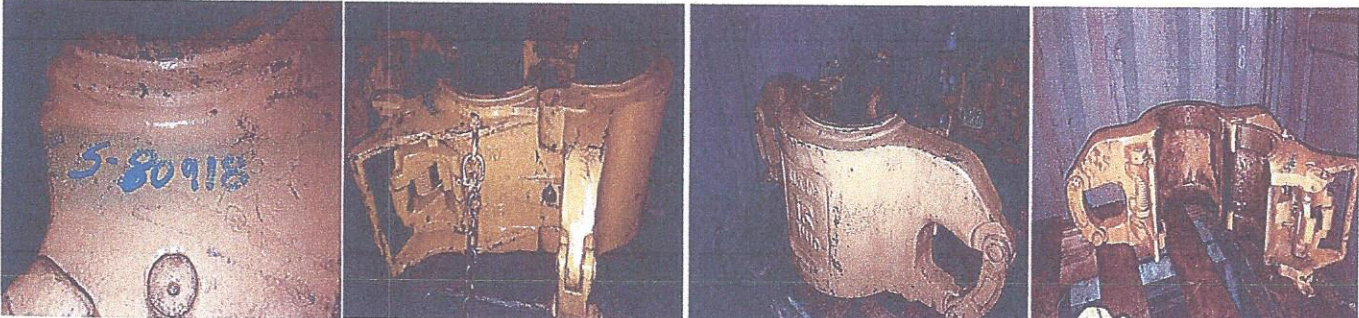



Ideal Inspection
 (a division of Ideal Oilfield Construction Ltd.)
 P.O Box 1473
 Brooks, Alberta
 T1R 1C3
 Phone: 403-362-2843 Fax: 403-362-2862

INSPECTION REPORT

Client: 4 Star Ventures		Location: DaPaJo Construction Limited		Date: October 21, 2014	
Page: 1 of 1		Unit :80918		Inspection: Magnetic Particle	
Work Order:2520G		Report:4273			
Parts Examined: 5 1/2" SLX 100 Casing Elevator					
Surface Condition: Painted			Material Temperature: 18° Celsius		
Procedure: MPI-DPJ-001			Code: ASME Section V, ASTM E709		
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets					
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method					
Test Medium: Magnaglo 14AM prepared bath					
Test Results:			Engineer's Approval:		
No cracks found at time of inspection					
Photos:					
					
Technician: Bryan Hoskins		CGSB #: 19053		Signature: 	
Assistant: Travis Bungay					
Repairs Complete		Yes <input type="checkbox"/> No <input type="checkbox"/>		N/A <input checked="" type="checkbox"/> X <input type="checkbox"/>	
Acceptable For Service				Yes <input checked="" type="checkbox"/> X <input type="checkbox"/> No <input type="checkbox"/>	
