


5 1/2 with 4 1/2 inserts

407



Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473
Brooks, Alberta
T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

INSPECTION REPORT

Client: Four Star Ventures

Location: DaPaJo Construction Limited

Date: April 05, 2012

P.O. :

Work Order : 2139j

Report : 3480

Page : 1 of 1

Rig or Unit : #7 C

Inspection: Magnetic Particle

Parts Examined: 4 1/2" M-W SLX 50 Ton elevator

S/N: 50500129

Surface Condition: Painted

Material Temperature: 20° Celsius

Procedure: MPI-DPJ-001

Code: ASME Section V, ASTM E709

Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets



Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method

Test Medium: Magnaflix 7HF prepared bath

Test Results:

Engineer's Approval:

No defects found at time of inspection.




**PERMIT TO PRACTICE
FIRTH ENGINEERING LTD.**

Signature:

Date: 05 April 2012

PERMIT NUMBER: P 6554
The Association of Professional Engineers,
Geologists and Geophysicists of Alberta

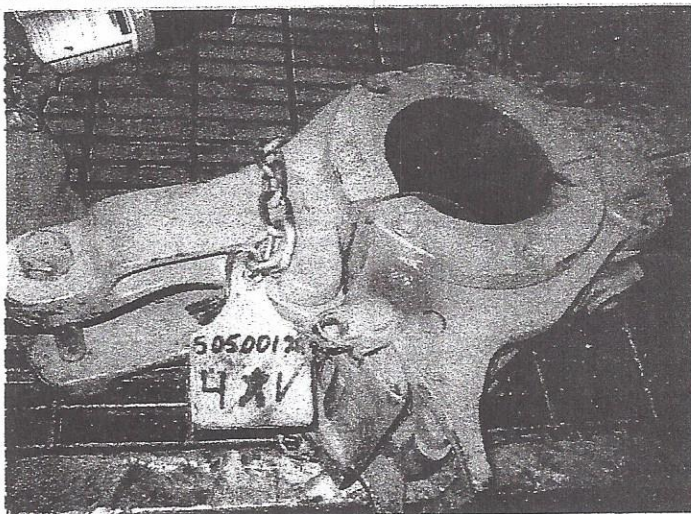

Photos:

| | | | | | | | | |
|------------------|--------------|---------|------|------------|------------------------|------------|---------------|----|
| Technician: | John Frances | CGSB #: | 7062 | Signature: | | Assistant: | Tyler Nevison | |
| Repairs Complete | Yes | No | N/A | X | Acceptable For Service | Yes | X | No |
