

Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473

Brooks, Alberta

T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

INSPECTION REPORT

Client: Four Star Ventures

Location: DaPaJo Construction Limited

Date: April 05, 2012

P.O. :

Work Order : 2139I

Report : 3479

Page : 1 of 1

Rig or Unit : #2 B

Inspection: Magnetic Particle

Parts Examined: 8 5/8" NOI 50 Ton elevator

S/N: TOP 74213

Surface Condition: Painted

Material Temperature: 20° Celsius

Procedure: MPI-DPJ-001

Code: ASME Section V, ASTM E709

Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets


Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method

Test Medium: Magnaflux 7HF prepared bath

Test Results:

Engineer's Approval:

No defects found at time of inspection.




PERMIT TO PRACTICE
FIRTH ENGINEERING LTD.

Signature:

Date:

PERMIT NUMBER: P 6554
 The Association of Professional Engineers,
 Geologists and Geophysicists of Alberta

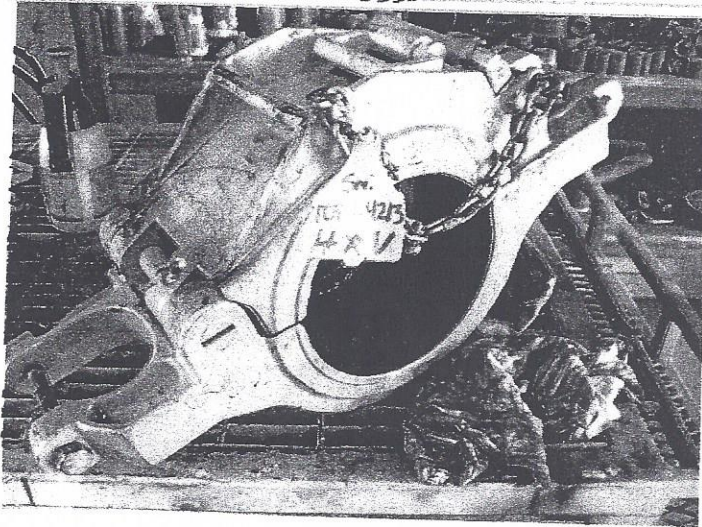

Photos:

Technician: John Frances

CGSB #: 7062

Signature: _____

Assistant: Tyler Nevison

Repairs Complete: Yes No N/A X

Acceptable For Service: Yes X No
