


Ideal Inspection
 (a division of Ideal Oilfield Construction Ltd.)
 P.O Box 1473
 Brooks, Alberta
 T1R 1C3
 Phone: 403-362-2843 Fax: 403-362-2862

INSPECTION REPORT

Client: Four Star Ventures	Location: DaPaJo Construction Limited	Date: April 05, 2012
P.O. :	Work Order : 2139p	Report : 3486
Page : 1 of 1	Rig or Unit :#3	Inspection: Magnetic Particic
Parts Examined: 9 5/8" NOI SLX 50 Ton elevator	S/N: TOP 74215	
Surface Condition: Painted	Material Temperature: 20° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe, PM-50 Permanent Magnets		
Method: Magnetic Particle, AC Continuous, Wet Colour Contrast Method		
Test Medium: Magnaflux 7HF prepared bath		

Test Results:
 No defects found at time of inspection.

Engineer's Approval:




**PERMIT TO PRACTICE
 FIRTH ENGINEERING LTD.**

Signature:

Date:

PERMIT NUMBER: P 6554
 The Association of Professional Engineers,
 Geologists and Geophysicists of Alberta

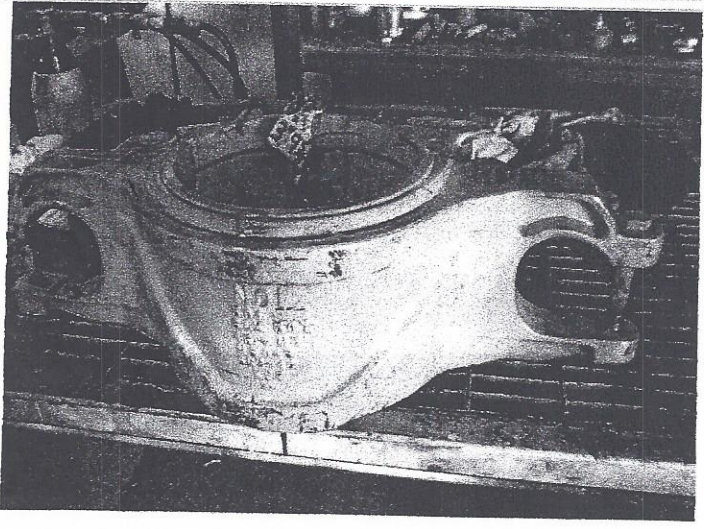

Photos:

Technician: John Frances	CGSB #: 7062	Signature:	Assistant: Tyler Nevison
Repairs Complete	Yes <input type="checkbox"/> No <input type="checkbox"/> N/A <input type="checkbox"/> X <input checked="" type="checkbox"/>	Acceptable For Service Yes <input type="checkbox"/> X <input checked="" type="checkbox"/> No <input type="checkbox"/>	
